



ASSAM POWER DISTRIBUTION COMPANY LIMITED.
OFFICE OF THE CHIEF GENERAL MANAGER (D & S),
(LOWER ASSAM REGION)
CIN: U40109AS2003SGC007242

No CGM (D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/ 66

Date: 07/07/2026

To,

M/s U.K. Enterprise,
R.P. Road, Dispur

Sub: **Approval of GTP and drawings.**

Ref: 1. Letter received from CGM(PP&D) vide No. CGM(PP&D)/APDCL/GTPA/PART-22/2025-26/4729 dated 02/07/2026.
2. Letter received from M/s U.K. Enterprise, R.P. Road, Dispur vide letter no. UAE/BMC/2026-27/146 dated: 24.06.2026

With reference to the above subject, this is to inform you that GTP along with drawings of item mentioned below is hereby approved subject to the strict compliance to the highlighted corrections and recommendations of the GTP. All factory accepted tests shall be conducted upon the item and submitted along with supply and verified before installation. The date of manufacturing of the said item should be after the date of issue of this letter.

➤ GTP for the following items have been approved.

Sl. No.	Description of item	Vendor Details
1	LT Pin Insulator	M/s Bikener Porcelain Pvt.Ltd, F-179-180, Bichwal Ind. Area, Bikaner, Rajasthan
2	HT Guy Insulator	
3	11KV Polymeric Disc Insulator, 70KN, T&C	
4	33KV Pin Insulator, Polymeric	
5	11KV Pin Insulator, Polymeric	

- N.B:**
1. *It is to be noted that this approval is solely against the furnished GTP of the said material and shall not be treated as approval of vendor under APDCL.*
 2. *All Tests Certificates are to be submitted along with the supply.*

Encl: - Approved GTPs.

Yours faithfully

Chief General Manager (D&S)

Memo No CGM (D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/

Date:

Copy to:

1. The CGM(PP&D), APDCL, Bijulee Bhawan, Paltanbazar, Ghy-01 for your information.
2. The CEO, Bongaigaon-EC, APDCL, LAR for information and necessary action.
3. Relevant File

Chief General Manager (D&S)



অসম শক্তি বিতৰণ কোম্পানী লিমিটেড
ASSAM POWER DISTRIBUTION COMPANY LIMITED
[CIN / চিআইন- U40109AS2003SGC007242]

No : CGM(PP&D)/APDCL/GTPA/PART-22/2025-26/ 4729

Dated : 02/07/2026

To,

Chief General Manager (LAR)
5th Floor, Bijulee Bhawan
Paltan bazar, Guwahati-1.

Sub: Approval of GTP

Ref: i) Letter No, CGM(D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/60, Dated:29.06.26

Sir,

With reference to the subject cited above, it is to inform you that the GTP along with drawings submitted from your end vide under Ref: i) have been scrutinized by the technical team of the office of the undersigned and the following items are hereby approved subject to full compliance to the highlighted corrections and recommendations. Details of materials:

Sl No.	Item Description	Manufacture
1	LT Pin Insulator	M/S Bikaner Porcelain Pvt. Ltd. Bikaner
2	HT Guy Insulator	
3	11KV Polymeric Disc Insulator 70KN, T&C	
4	33KV Pin Insulator, Polymeric	
5	11KV Pin Insulator, Polymeric	

Moreover, you are also requested to ensure that the approved item supplied strictly comply with the approved GTP & highlighted corrections/recommendations. All factory acceptance tests shall be conducted upon the item. The date of manufacture of the said item shall be later than the date of issue of this letter.

This is for favour of your kind information and necessary action.

Yours sincerely

Chief General Manager (PP&D)



ASSAM POWER DISTRIBUTION COMPANY LIMITED.

OFFICE OF THE CHIEF GENERAL MANAGER (D).

(LOWER ASSAM REGION)

CIN: U40109AS2005SGC007242

No. CGM (D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/ 60

Date: 29/6/2026

To,

The Chief General Manager (PP&D),
APDCL, Bijulee Bhawan, 7
Paltan Bazar, Guwahati-1.

WJM, PWD

ACM/DM
T&C Circle
B

Sub: Forwarding of GTP & Drawing

Ref: 1. Letter received from M/s U.K. Enterprise, R.P. Road, Dispur, vide No. UKE/BMC/2026-27/146 dated: 24.06.2026.

Sir,

With reference to the above subject, enclosed please find herewith a letter received from M/s U.K. Enterprise, R.P. Road, Dispur regarding submission of GTP and drawings of following materials for the work Construction of 33KV Dedicated Medical College Feeder from 132KV/33KV Dhaligaon GSS to the premises of Bongaigaon Medical College, Maigaon and associated works under Bongaigaon-ESD-I against LoA issued vide No. CGM(D&S)/APDCL/LAR/ Bongaigaon Medical College /2025-2026/38 dated: 13.05.2026 for your information and necessary action.

Details are as follows :-

Sl. No.	Description of item	Vendor Details
1	LT Pin Insulator	M/s Bikener Porcelain Pvt.Ltd, F-179-180, Bichwal Ind. Area, Bikaner, Rajasthan
2	HT Guy Insulator	
3	11KV Polymeric Disc Insulator, 70KN, T&C	
4	33KV Pin Insulator, Polymeric	
5	11KV Pin Insulator, Polymeric	

To (DMC) PWD review put up 30/6

Encl:- 1. Copy of letter under Reference.
2. GTP and Drawing



Yours faithfully

Chief General Manager (D&S)
APDCL, LAR



M/S. U.K. ENTERPRISE

Govt. Approved (Class I) Contractor,

Deals with all Electrical, Civil works & Consultant

UDYAM REGISTRATION NO. UDYAM-AS-03-0005077

Dr. R.P. Road, Dispur, Guwahati-781006, Ph.98643-46349, 90853-90161 Email: babultalukdar@gmail.com

No. UKE/ BMC/2026-27/ 146

Date 24.06.2026

To

The Chief General Manager(D&S)
APDCL (LAR), Bijulee Bhawan,
Paltan Bazar, Guwahati -1

Sub:- Approval of GTP and Drawing

Ref:- 1. LOA No. CGM(D&S)/APDCL/LAR/Bongaigaon Medical College /2025-26/38
Dt. 13.05.2026

Sir,

With reference to the above, we have the honour to forward herewith the GTP and Drawing of the following materials for favour of according necessary approval from your end.


The details are as follows :-

Sl. No.	Item Description	Name of Manufacturer	Remarks
1	LT Pin Insulator	M/s. Bikaner Porcelain Pvt. Ltd., F-179-18, Bichwal Industrial Area, Bikaner-334005, Rajasthan (India)	
2	HT Guy Insulator		
3	11 KV Polymeric Disc insulator, 70 KN, T&C		
4	33 KV Pin insulator, Polymeric		
5	11 KV Pin Insulator, Polymeric		

The above materials will be utilised for Construction of 33kV Dedicated Medical College Feeder from 132/33kV Dhaligaon GSS to the premises of the Bongaigaon Medical College, Majgaon and associated work under Bongaigaon ESD-I under Deposit Work Scheme

Thanking you in anticipation and assuring our best service in future.

Encl. : As above



Handwritten signature: chandhary DmG

Yours faithfully
Authorised Signatory

M/S. U.K. Enterprise,
Dispur, Guwahati -06

Handwritten signature: CGM (D&S) APDCL (LAR)



BIKANER PORCELAIN PVT. LTD.



Client	ASSAM POWER DISTRIBUTION COMPANY LIMITED
Project	Bongaigaon Medical College
Name of Work	Construction of 33kV dedicated Medical College feeder from 132/33 kV Dhaligaon GSS to the premises of the Bongaigaon Medical College, Majgaon and Associated Work under Bongaigaon ESD-I under Deposit Work Scheme
Work Order No.	CGM(D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/38 date : 13.05.2026
Contractor	M/S UK Enterprises
Manufacturer	M/S. BIKANER PORCELAIN PVT. LTD., BIKANER (Raj.)
Drawing No.	BPPL-LT-05
Materials	LT PIN INSULATOR

GUARANTEED TECHNICAL PARTICULARS - LT PIN INSULATORS (TYPE I)

S.No.	Particulars	Guaranteed Value
01.	NAME OF SUPPLIER AND ADDRESS	M/s. Bikaner Porcelain P. Ltd., F-179-180, Bichwal Ind. Area, Bikaner
02.	Type of Insulators	Type I
03.	Standards to which insulators will conform	IS: 1445/1977 Latest amendment
04.	Dimensions	70 mm X 100 mm
05.	Color of Glaze	Brown
06.	Dry Power freq. Withstand voltage (KV)	23 KV
07.	Wet Power freq. Withstand voltage (KV)	10 KV
08.	Puncture Withstand Voltage	1.3 times of actual Dry Flashover Voltage
09.	Minimum failing Load (KN)	3.5 KN
10.	Temp Cycle test (as per ISS)	As per clause 7.8 of IS 1445
11.	Porosity test (as per ISS)	As per clause 7.11 of IS 1445
12.	Packing details	In HDP bags wrapped in grass/ Corrugated box
13.	Furnished drawing no.	BPPL-LT-05
14.	Marking Detail	BPPL, Year of Manufacturing

④ All tests certificates to be submitted along with supply.

DM (T&C) OP&D
PP&D, APDCL

DM (T&C) OP&D
PP&D, APDCL



Agnes Dikhorug
GM (PP&D)
APDCL

For Bikaner Porcelain Pvt. Ltd

(Authorised Signatory)






BIKANER PORCELAIN PVT. LTD.



Client	ASSAM POWER DISTRIBUTION COMPANY LIMITED
Project	Bongaigaon Medical College
Name of Work	Construction of 33kV dedicated Medical College feeder from 132/33 kV Dhaligaon GSS to the premises of the Bongaigaon Medical College, Majgaon and Associated Work under Bongaigaon ESD-I under Deposit Work Scheme
Work Order No.	CGM(D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/38 date : 13.05.2026
Contractor	M/S UK Enterprises
Manufacturer	M/S. BIKANER PORCELAIN PVT. LTD., BIKANER (Raj.)
Drawing No.	BPPL-LT-05
Materials	LT PIN INSULATOR

LT PIN INSULATOR

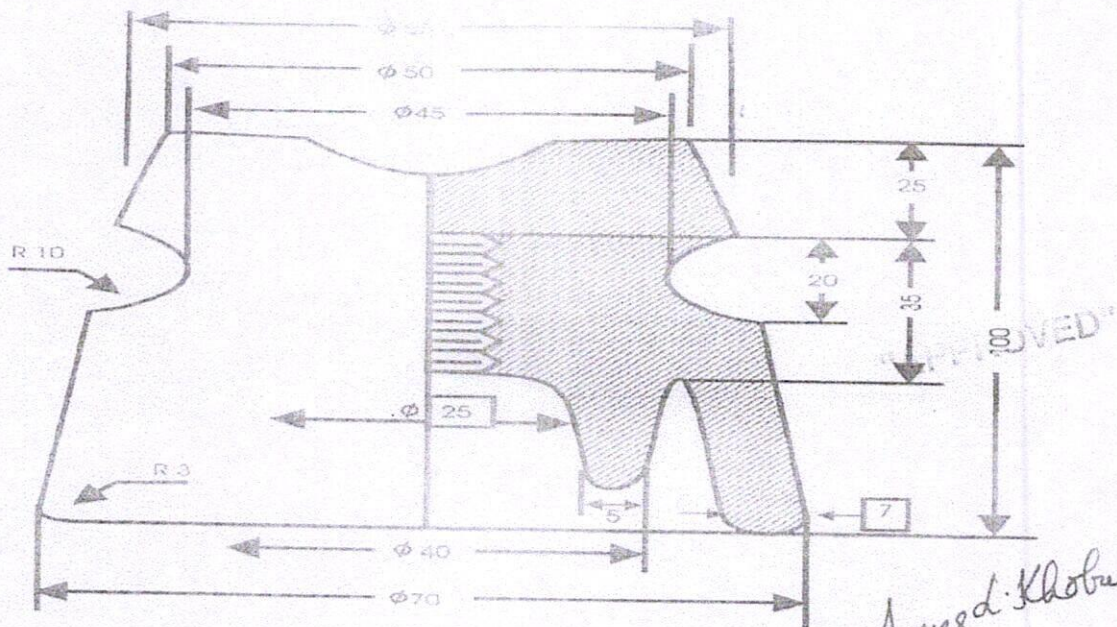

Agnes d. Khobung
GM (PP&D)
APDCL

6. IS SPECIFICATION

LT PIN INSULATOR - TYPE I (70mmX100mm)

DRAWING No. BPPL-LT-05

CHECKED By:

APPROVED By:

DM
DM (T&C Circle)
PP&D, APDCL

AGM
AGM (T&C Circle)
PP&D, APDCL



For Bikaner Porcelain Pvt. Ltd

M. V. Patel
(Authorised Signatory)





BIKANER PORCELAIN PVT. LTD.



Client	ASSAM POWER DISTRIBUTION COMPANY LIMITED
Project	Bongaigaon Medical College
Name of Work	Construction of 33kV dedicated Medical College feeder from 132/33 kV Dhaligaon GSS to the premises of the Bongaigaon Medical College, Majgaon and Associated Work under Bongaigaon ESD-I under Deposit Work Scheme
Work Order No.	CGM(D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/38 date : 13.05.2026
Contractor	M/S UK Enterprises
Manufacturer	M/S. BIKANER PORCELAIN PVT. LTD., BIKANER (Raj.)
Drawing No.	BPPL-HT-01
Materials	33KV/HT GUY INSULATOR TYPE-C

GUARANTEED TECHNICAL PARTICULARS HT GUY INSULATOR [TYPE-C]

S. No.	Description	Particulars
1	Manufacturer's Name & Address	Bikaner Porcelain Pvt. Ltd. F-179-180, Bichwal Industrial Area, Bikaner
2	Type of Insulator offered	Type -C
3	Standards to which insulator will conform	IS : 5300/1969 Latest amendment
4	Dimensions	140mm x 85mm x 25mm
5	Hole diameter (mm)	25 + 1.5mm
6	Colour of glaze	Brown
7	Dry Power Frequency withstand voltage (kV)	27KV
8	Wet Power Frequency withstand voltage (kV)	13KV
9	Minimum failing load (Newton)	88KN
10	Minimum Creepage distance (mm)	57MM
11	Weight per piece (Kg.)	1.2 Kg (APPROX)
12	Temperature cycle test (as per ISS)	As per clause 7.6 of IS 5300
13	Porosity test (as per ISS)	As per clause 7.7 of IS 5300
14	Tolerance, if any (as per ISS)	As per ISS
15	Marking detail	BPPL, Year of Manufacturing

⊗ All tests certificate to be submitted alongwith supply

DM (T&C Circle)
PP&D, APDCL

AGM (T&C Circle)
PP&D, APDCL

AGM (PP&D)
APDCL

For Bikaner Porcelain Pvt. Ltd.

(Authorised Signatory)







BIKANER PORCELAIN PVT. LTD.



Client	ASSAM POWER DISTRIBUTION COMPANY LIMITED
Project	Bongaigaon Medical College
Name of Work	Construction of 33kV dedicated Medical College feeder from 132/33 kV Dhaligaon GSS to the premises of the Bongaigaon Medical College, Majgaon and Associated Work under Bongaigaon ESD-I under Deposit Work Scheme
Work Order No.	CGM(D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/38 date : 13.05.2026
Contractor	M/S UK Enterprises
Manufacturer	M/S. BIKANER PORCELAIN PVT. LTD., BIKANER (Raj.)
Drawing No.	BPPL-HT-01
Materials	33KV/HT GUY INSULATOR TYPE-C

HT GUY INSULATOR (TYPE C)

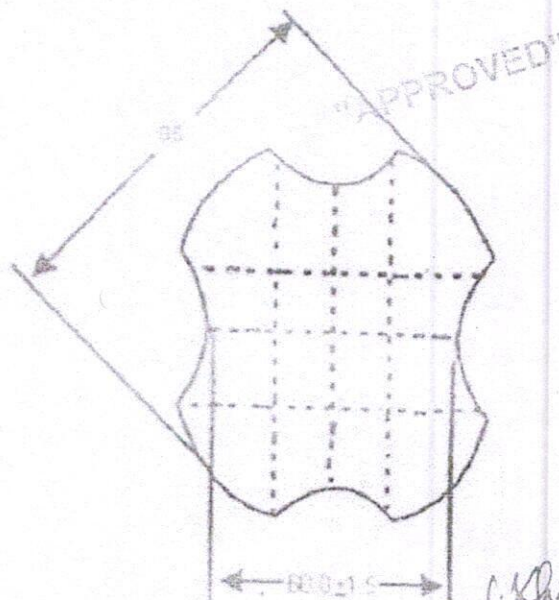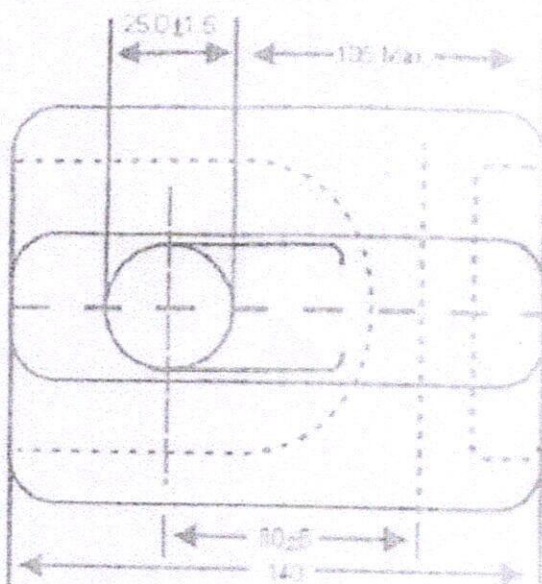

Agnes Kholung
GM (PP&D)
APDCL

BIKANER PORCELAIN PVT. LTD., BIKANER

33KV/HT GUY INSULATOR - TYPE C (140mmX85mmX25mm)

DRAWING No. BPPL-HT-01

CHECKED By:

APPROVED By:

for
DM (T&C Circle)
PP&D, APDCL

for
ADM (T&C Circle)




For Bikaner Porcelain Pvt. Ltd

M. Anand
(Authorised Signatory)



Client	ASSAM POWER DISTRIBUTION COMPANY LIMITED
Project	Bongaigaon Medical College
Name of Work	Construction of 33kV dedicated Medical College feeder from 132/33 kV Dhaligaon GSS to the premises of the Bongaigaon Medical College, Malgaon and Associated Work under Bongaigaon ESD-I under Deposit Work Scheme
Work Order No.	CGM/D&S/APDCL/LAR/Bongaigaon Medical College/2025-26/38 date : 13.05.2026
Contractor	M/S UK Enterprises
Manufacturer	M.S. BIKANER PORCELAIN PVT. LTD., BIKANER (Raj.)
Drawing No.	BPP/L/11KV/DISC/T&C/01
Materials	11KV / 70KN, COMPOSITE POLYMER DISC INSULATOR (T&C Type)



TECHNICAL CHARACTERISTICS

DIMENSIONS

1. ARGING DISTANCE = 165mm
2. CREEPAGE DISTANCE = 320mm

MECHANICAL CHARACTERISTIC

1. MINIMUM FAILING LOAD = 45KN
2. COLOR = GRAY/LIGHT GRAY

ELECTRICAL CHARACTERISTICS

1. RATED SYSTEM VOLTAGE = 11KV (rms)
2. HIGHEST SYSTEM VOLTAGE = 12KV (rms) 3. WET ONE MINUTE POWER FREQUENCY WITHSTAND VOLTAGE = 35KV (rms)
4. DRY LIGHTING IMPULSE WITHSTAND VOLTAGE = 75KV
5. RATED FREQUENCY = 50 HZ

DIMENSION CHART

	A	B	C	D
DIMENSION AS PER DRAWING	Ø100	Ø22	Ø16	Ø44
TOLERANCE AS PER IEC 61109	±5.5	±2.72	±2.14	±3.26

NOTE:

1. INSULATOR CONFORMS TO IEC 61109 - 1992/2008 IS 16684 : 2018 IS 2486-1974 & LATEST EDITION
2. GALVANIZATION CONFORMS TO IS 2633/IS 2629-1985
3. ALL DIMENSIONS ARE IN mm
4. DIMENSION TOLERANCE AS PER IEC 61109

* + (0.04xd+1.5)MM when d < 300mm

* + (0.025xd+6)MM when d > 300mm


Drawn by M.P. Singh
Checked by M.P. Singh
Approved by S.M. Munda



Bikaner Porcelain Pvt. Ltd.
F-179-180, Bichwal Industrial Area
Bikaner - 334 005 - Rajasthan (India)

ITEM NAME
11KV 70KN COMPOSITE POLYMER DISC INSULATOR (T&C TYPE)

DRG. NO. BPP/L/11KV/DISC/T&C/01



FIRST ANGLE PROJECTION

S No	DESCRIPTION
1	CLEVIS FITTING - SGG/MCU/C/PPRGOMG
2	COTTER PIN - SGG/MCU/C/PPRGOMG
3	CORE ROD - FRP ROD
4	POLYMER HOUSING - SILICON RUBBER
5	TONGUE FITTING - SGG/MCU/C/PPRGOMG
6	SPLIT PIN - SS/MS/BRONZE/COPPER

For Bikaner Porcelain Pvt. Ltd.
(Authorised Signatory)

M. P. Singh

APDCL (PP&D)
APDCL

APDCL (PP&D)
APDCL

APDCL (PP&D)
APDCL

APDCL (PP&D)
APDCL



BIKANER PORCELAIN PVT. LTD.



Client	ASSAM POWER DISTRIBUTION COMPANY LIMITED
Project	Bongaigaon Medical College
Name of Work	Construction of 33kV dedicated Medical College feeder from 132/33 kV Dhaligaon GSS to the premises of the Bongaigaon Medical College, Majgaon and Associated Work under Bongaigaon ESD-I under Deposit Work Scheme
Work Order No.	CGM(D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/38 date : 13.05.2026
Contractor	M/S UK Enterprises
Manufacturer	M/S. BIKANER PORCELAIN PVT. LTD., BIKANER (Raj.)
Drawing No.	BPPL/33kV/10kN/Pin/01
Materials	33KV 10KN COMPOSITE POLYMER PIN INSULATOR

GUARANTEED TECHNICAL PARTICULARS OF 33KV, 10KN, COMPOSITE POLYMER PIN INSULATOR

S. No.	Parameter/Description	Offered
i)	RIV at 1 Mhz when energized at 10KV (rms) under dry condition (Microvolt)	Less than 100 Microvolts
ii)	Min. Creepage Distance (mm)	900
8.	Mechanical failing load KN (Min.)	10
9.	Dimensions:	
a)	Weight of Insulator	1.8 Kg. (Approx)
b)	Diameter of FRP Rod (mm)	24 ± 2.46MM
c)	Length of FRP Rod (mm)	>395
d)	Diameter of weather sheds (mm)	100 ± 5.5MM
e)	Thickness of Housing (mm)	3
f)	Dry Arc Distance min. (mm)	390
g)	Length of bottom end fitting	130 MM2
10.	Dimensioned drawing of insulator (including weight with tolerance in weight) enclosed	Yes Drawing No. BPPL/33KV/10KN/PIN/01
11.	Method of fixing of sheds to housing: Single mould or modular construction (injection moulding/compression moulding)	Single Injection moulding
12.	No. of weather threads	08
13.	Type of sheds	
a)	Aerodynamics	Yes, Aerodynamics
b)	With Under Ribs	No
14.	Packing details: Type of packing No. of Insulator in each pack Gross weight of each pack	HDPE Bags/ Corrugated Boxes Min. 12 max. 40 Nos. of Insulators in each pack ≤ 50Kgs.

② All test certificates to be submitted along with supply.

DM (T&C Circle)
PP&D, APDCL

AGM (T&C Circle)
PP&D, APDCL


Agnes L. Khobragade
DM (PP&D)
APDCL

For Bikaner Porcelain Pvt. Ltd.

Authorised Signatory



Client	ASSAM POWER DISTRIBUTION COMPANY LIMITED
Project	Bongaigaon Medical College
Name of Work	Construction of 33KV dedicated Medical College feeder from 132/33 KV Dhaligaon GSS to the premises of the Bongaigaon Medical College, Majgaon and Associated Work under Bongaigaon ESD-I under Deposit Work Scheme
Work Order No.	CGM/D&S/APDCL/LAR/Bongaigaon Medical College/2025-26/38 date : 13.05.2026
Contractor	M/S UK Enterprises
Manufacturer	M/S. BIKANER PORCELAIN PVT. LTD., BIKANER (Raj.)
Drawing No.	BPPL/33KV/10KN/Pin/01
Materials	33KV 10KN COMPOSITE POLYMER PIN INSULATOR

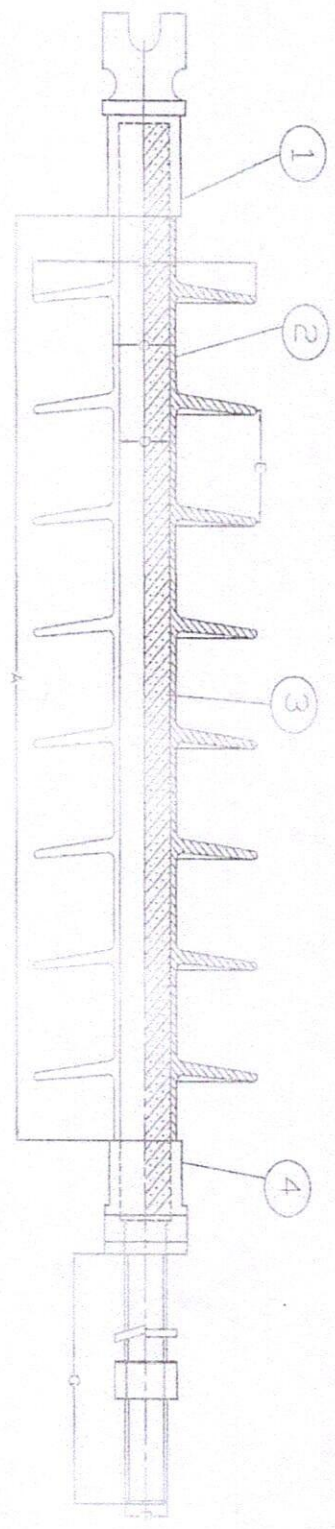

APPLICABLE STANDARDS

DIMENSION CHART

	A	B	C	D	E	F	G	S. No.	DESCRIPTION
DIMENSION AS PER DRAWING	365	Ø100	Ø31	Ø24	Ø44	20/24	330/250/250	1.	TECHNICAL DETAIL
TOLERANCE AS PER IEC 61109	+15.13	+5.5	+2.74	+2.26	+3.26			2.	WATER FILLING TOP - SGL/MCL/ROUNDED
								3.	MATERIAL OF HOUSING - HTV SI CON AT 185N
								4.	MATERIAL OF FRP ROD - ECR GR44 - FRP
								5.	MATERIAL FITTING BOTTOM - SGL/MCL/ROUNDED

S.NO.	DESCRIPTION	MATERIAL
01.	METAL FITTING TOP	SGL/MCL
02.	POLYMER HOUSING	SILICON RUBBER
03.	CORE ROD	FRP ROD
04.	METAL FITTING BOTTOM	SGL/MCL
05.	STUD, NUT & WASHER	SGL/MCL/ROUNDED

TOLERANCE
 $\pm (0.04 \times d + 1.5)$ mm when $d < 300$ mm
 $\pm (0.025 \times d + 6)$ mm when $d < 300$ mm

APPROVED

For Bikaner Porcelain Pvt. Ltd
 (Authorized Signatory)

Drawn by M.P. Singh		Bikaner Porcelain Pvt. Ltd. F-179-180, Bichwal Industrial Area Bikaner - 334 005 - Rajasthan (India)	ITEM NAME 33KV 10KN COMPOSITE POLYMER PIN INSULATOR	DRG. NO. BPPL/33KV/10KN/PIN/01
Checked by M.P. Singh				FIRST ANGLE PROJECTION
Approved by S.M. Mundhra				

DM (TCC Circle)
 PRED. APDCL

James E. H. H. H. H.
 DM (PP&D)
 APDCL

RISE



BIKANER PORCELAIN PVT. LTD.



Client	ASSAM POWER DISTRIBUTION COMPANY LIMITED
Project	Bongaigaon Medical College
Name of Work	Construction of 33kV dedicated Medical College feeder from 132/33 kV Dhaligaon GSS to the premises of the Bongaigaon Medical College, Majgaon and Associated Work under Bongaigaon ESD-I under Deposit Work Scheme
Work Order No.	CGM(D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/38 date : 13.05.2026
Contractor	M/S UK Enterprises
Manufacturer	M/S. BIKANER PORCELAIN PVT. LTD., BIKANER (Raj.)
Drawing No.	BPPL/11KV/05KN/PIN/01
Materials	11KV, 05KN, COMPOSITE POLYMER PIN INSULATOR

GUARANTEED TECHNICAL PARTICULARS OF 11KV, 05KN, COMPOSITE POLYMER PIN INSULATOR

S. No.	Parameter/Description	Offered
1.	Name of Manufacturer	Bikaner Porcelain Pvt. Ltd.
2.	Address	F-179-180, Bichwal Ind. Area, Bikaner- 334 006
a)	Registered Office	--- AS ABOVE ---
b)	Factory	--- AS ABOVE ---
3.	Type of insulators	Composite Polymeric Insulator
4.	Standard according to which insulators are manufactured & tested	IEC 61109 - 2008
5.	Name of material used for manufacturer of the insulator	
a)	Material of core rod (FRP) i) E-Glass or ECR-glass ii) Boron Content	ECR-glass fiber, Boron Free
b)	Material of housing & weather sheds (silicon content by weight) i) Housing ii) Weather Sheds	Silicon Rubber Silicon Content - Min 30% by weight
c)	Material of end fitting	SGCI/MCI
d)	Sealing compound for end fittings	RTV Silicon Sealant
6.	Colour Glaze of Insulator	Gray/Light Grey
7.	Electrical characteristics :	
a)	Nominal system voltage (kVrms)	11
b)	Highest system voltage (kVrms)	12
c)	Dry Power frequency withstand voltage (kVrms)	75
d)	Wet power frequency withstand voltage (kVrms)	45
e)	Dry Power frequency flashover voltage (kVrms)	80
f)	Wet Power frequency flash over voltage (kVrms)	50
g)	Dry lighting impulse withstand voltage a) Positive (kV peak) b) Negative (kV peak)	110 110
h)	Dry lighting impulse flashover voltage c) Positive (kV peak) d) Negative (kV peak)	125 125
i)	RIV at 1 Mhz when energized at 10KV kv (rms) under dry condition (uV)	Less than 100 micro volts
j)	Creepage Distance min. (mm)	320

"APPROVED"

Agnes K. K. K.
DM (PP&D)
APDCL

* All test certificates to be submitted with supply.


DM (T&C Circle)
PP&D, APDCL

Regd. Office & Works : F-179-180, Bichwal Industrial Area, Bikaner - 334006
E-mail : info@bikanerporcelain.in CIN No. : U14100RJ1990PTC005406

AGM (PP&D)
APDCL



Client	ASSAM POWER DISTRIBUTION COMPANY LIMITED
Project	Bongaigaon Medical College
Name of Work	Construction of 33kV dedicated Medical College feeder from 132/33 kV Dhaligaon GSS to the premises of the Bongaigaon Medical College, Majaon and Associated Work under Bongaigaon ESD-1 under Deposit Work Scheme
Work Order No.	CGM(D&S)/APDCL/LAR/Bongaigaon Medical College/2025-26/38 date : 13.05.2026
Contractor	M/S UK Enterprises
Manufacturer	M/S. BIKANER PORCELAIN PVT. LTD., BIKANER (Raj.)
Drawing No.	BPPL/11KV/05KN/PIN/01
Materials	11KV, 05KN, COMPOSITE POLYMER PIN INSULATOR

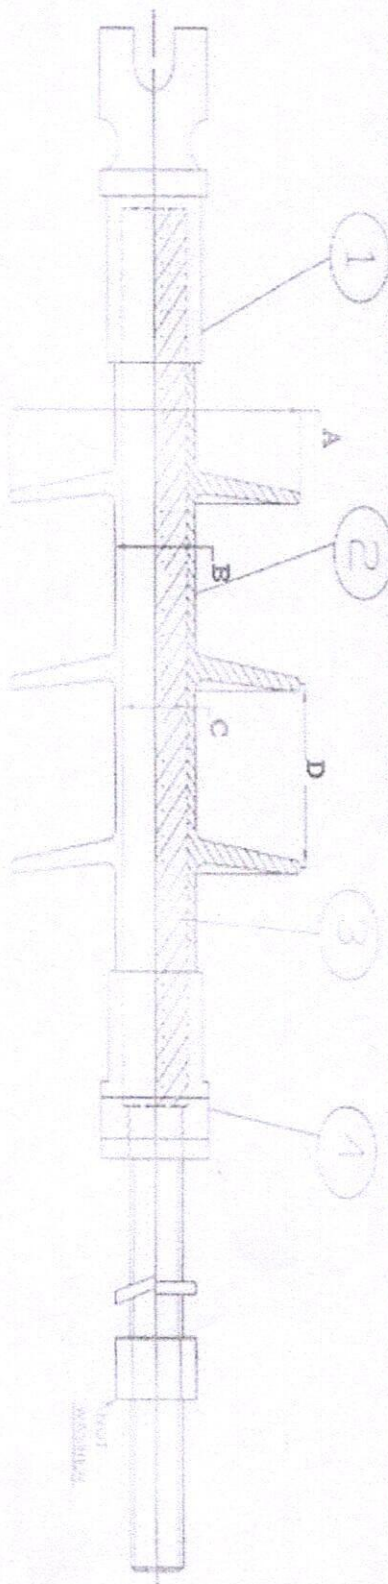

TECHNICAL CHARACTERISTICS

DIMENSION CHART

- DIMENSIONS**
1. ARcing DISTANCE = 165MM
 2. CREEPAGE DISTANCE = 320MM (Minimum)
- MECHANICAL CHARACTERISTIC**
1. MINIMUM FAILING LOAD = 05KN
 2. COLOR = GRAY/LIGHT GRAY

ELECTRICAL CHARACTERISTICS

1. RATED SYSTEMS VOLTAGE = 11KV (rms)
2. HIGHEST SYSTEMS VOLTAGE = 12KV (rms)
3. WET ONE MINUTE POWER FREQUENCY WITHSTAND VOLTAGE = 40KV (rms)
4. DRY LIGHTING IMPULSE WITHSTAND VOLTAGE = 110 KVP
5. RATED FREQUENCY = 50 Hz

NOTE:	A	B	C	D
1. INSULATOR CONFORMS TO IEC: 61109 - 1992/2008	Ø100	Ø30	Ø24	Ø44
2. GALVANIZATION CONFORMS TO IS 2633/IS2629-1985	+5,5	+2,70	+2,46	+3,26
3. ALL DIMENSIONS ARE IN mm				

1. RATED SYSTEMS VOLTAGE = 11KV (rms)

2. HIGHEST SYSTEMS VOLTAGE = 12KV (rms)

3. WET ONE MINUTE POWER FREQUENCY WITHSTAND VOLTAGE = 40KV (rms)

4. DRY LIGHTING IMPULSE WITHSTAND VOLTAGE = 110 KVP

5. RATED FREQUENCY = 50 Hz

"APPROVED"



For Bikaner Porcelain Pvt. Ltd.

(Authorised Signatory)

Drawn by M.P. Singh		ITEM NAME	11KV 05KN COMPOSITE POLYMER PIN INSULATOR	DRG. NO. BPPL/11KV/05KN/PIN/01
Checked by M.P. Singh				
Approved by S.M. Mundhra				FIRST ANGLE PROJECTION

Bikaner Porcelain Pvt. Ltd.

F-179-180, Bichwal Industrial Area
Bikaner - 334 005 - Rajasthan (India)



Approved by
S.M. Mundhra
DM (PP&D)
APDCL

DM (T&C Circle)
PP&D, APDCL
